

Reson8 Platform — Master Roadmap

All Phases · All Modules · Sprint Plan · Build-Up Curve

Prepared by: ID8 Media · Product Engineering
Date: June 2026
Version: 1.0

1. Strategic Overview

Reson8 is delivered in three consecutive phases over six months. Every phase ends with a broadcast-ready release — not a milestone or a demo. Each release adds modules on top of a shared, stable Core.

Release Milestones

Release	End of	Modules Live	Cumulative P1 Features
R1	Month 2	Core + ORA Elections	64
R2	Month 4	+ ARENA Sports + FLASH Breaking News	113
R3	Month 6	+ PULSE Finance + ATMOS Weather	143

Full Platform Scope — All Phases

Layer	P1	P2	P3	∞	Total
Sentra Engine	—	—	—	12	12
Reson8 Core	24	4	—	5	33
ORA — Elections	31	21	5	—	57

Layer	P1	P2	P3	∞	Total
ARENA — Sports	25	10	3	—	38
PULSE — Finance & Markets	18	7	2	—	27
ATMOS — Weather	12	6	3	—	21
FLASH — Breaking News	16	4	2	—	22
Total	126	52	15	17	210

P1 delivery = 126 + 17 (∞) = 143 features

2. Team & Velocity

Role	Contribution
Technical Manager (14 years)	Architecture · code review · 60% development
Senior Developer 1	Full development
Senior Developer 2	Full development
Product Engineer	Requirements · UAT · delivery management
Product Manager	Scope · stakeholder · grooming

Effective development velocity: 26 dev-days per 2-week sprint

Per phase: 4 sprints × 26 dev-days = 104 dev-days

3. Why Elections First

Phase 1 is built on ORA Elections for four reasons:

1. **Fixed broadcast dates.** An election cannot wait for a late release. The platform must be ready before the broadcast date is set.
2. **ORA tests every platform capability.** Live data feeds, editorial chain, Vizrt graphics, breaking news detection, social sentiment, bilingual output — ORA exercises all of them. Proving ORA proves the Core.
3. **Core built for ORA is inherited by all modules.** Every architectural decision made in Phase 1 benefits Phase 2 and 3 directly. There is no rework.

4. **Commercial priority.** ORA is the flagship module. A working election broadcast system is the most compelling demonstration to any broadcaster.
-

4. Platform Architecture — Phase 1 Built for All Modules

The most critical architectural discipline of Phase 1: every technical decision is made with five modules in mind, not one.

Six infrastructure decisions made in Phase 1 that enable Phase 2 and Phase 3 without modification:

4.1 Module Registry

Each module (ORA · ARENA · PULSE · ATMOS · FLASH) is a self-contained domain package. It registers with Core at startup, declaring: - Its data feeds - Its entity types - Its event types - Its Vizrt template bindings

Adding a new module requires zero changes to Core code.

Phase 1 establishes this pattern with ORA. ARENA, FLASH, PULSE, and ATMOS register identically in Phases 2 and 3.

4.2 Feed Abstraction Layer (FAL)

A generic `DataFeedConnector` interface built in Phase 1 for ORA's official election results feed. Every future module uses the same interface — only the configuration changes.

Phase	Module	Feed Provider
Phase 1	ORA	Official election results API
Phase 2	ARENA	Opta / Stats Perform
Phase 2	FLASH	News wire APIs · Social APIs
Phase 3	PULSE	Bloomberg / Reuters / Exchange APIs
Phase 3	ATMOS	Tomorrow.io / AccuWeather / National Met

Interface: `authenticate()` · `subscribe(fields)` · `onUpdate(handler)` · `onFailure(fallback)`

Primary + fallback feed switching is handled by the FAL, not by individual modules.

4.3 Generic Event Pipeline

Every data event — regardless of module — flows through the same immutable processing chain:

Raw Feed Event


→ Ingest Service	<code>normalize schema</code> · <code>deduplicate</code>
→ Validation Service	<code>anomaly detection</code> · <code>hold-and-flag</code> (014 · A13 · F18)
→ Sentra Enrichment	<code>sentiment</code> · <code>classification</code> · <code>entity linking</code> · <code>NER</code>
→ Editorial Queue	C1 — Producer stages
→ Approval Gate	C2 · C7 — Editor reviews and approves
→ Take to Air	C3 — Operator fires to Vizrt
→ Audit Log	C6 · C21 — immutable record

Event types differ (`ELECTION_RESULT` · `MATCH_EVENT` · `MARKET_MOVE` · `WEATHER_ALERT` · `BREAKING_SIGNAL`). The pipeline is identical. **Built once in Phase 1. Reused across all modules.**

4.4 Extensible Entity Model

Entity types are defined with inheritance in Phase 1. Future modules extend the base schema without modifying existing types.

Entity (`id` · `name` · `type` · `metadata` · `media` · `social_handles`)

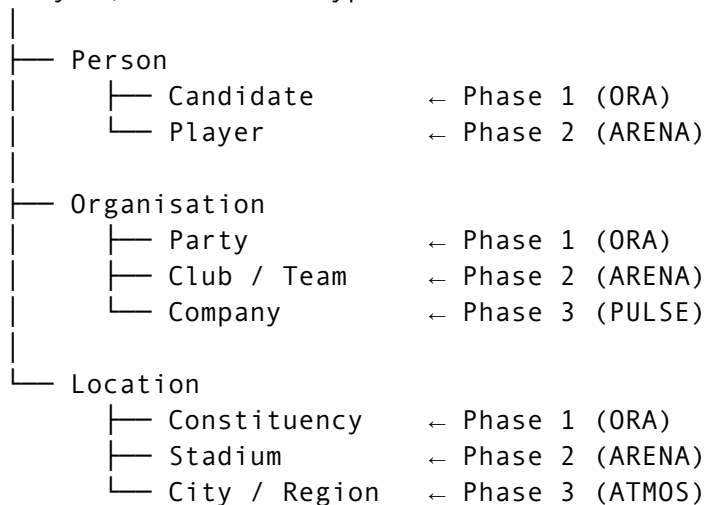

4.5 Vizrt Template Registry

A central registry maps: `module` → `event_type` → `scene_id` → `data_container_bindings`

Pipeline logic never hardcodes a Vizrt scene ID. It queries the registry.
Module templates are loaded at startup.

Phase	Module	Scenes Registered
Phase 1	ORA	Results bar · map · ticker · candidate card · seat projection
Phase 2	ARENA	Score bug · events panel · stats panel · player card · table
Phase 2	FLASH	Flash overlay · ticker · alert card · developing banner
Phase 3	PULSE	Ticker bar · price panel · index display · gainers/losers
Phase 3	ATMOS	Conditions card · forecast display · temperature map · alert overlay

4.6 Shared Sentra Engine Client

One authenticated connection to the Sentra Engine. Established in Phase 1 Sprint 1. All modules call the same client — no reconnection, no re-authentication in Phase 2 or 3.

Shared methods available to all modules: - `engine.sentiment(text, lang)` — multi-language sentiment scoring - `engine.classify(event)` — breaking · developing · routine classification - `engine.ner(text)` — named entity extraction - `engine.generate(template, data)` — headline · caption · bilingual broadcast copy

Architecture Summary

What is built in Phase 1	What it enables in Phase 2 & 3
Module Registry	

What is built in Phase 1	What it enables in Phase 2 & 3
	Add ARENA, FLASH, PULSE, ATMOS — zero Core changes
Feed Abstraction Layer	Plug in Opta, Bloomberg, weather APIs — same interface
Generic Event Pipeline	All module events processed identically — no new pipeline
Extensible Entity Model	Add Player, Company, City types — no schema breaking changes
Vizrt Template Registry	Register new module scenes at startup — no pipeline changes
Shared Sentra Engine Client	All modules use same Engine connection from day one

5. Full Sprint Plan — 12 Sprints · 24 Weeks

Phase 1 — Foundation + Core + ORA Elections (Weeks 1–8)

Sprint	Weeks	Focus	Dev 1 (TM + Senior)	Dev 2 (Senior)	Features
S1	1–2	Foundation	Infrastructure · CI/CD · Sentra Engine client · Vizrt SDK	Architecture · module registry · FAL skeleton · entity model	E1–E12 (12)
S2	3–4	Core: Editorial + Auth	Editorial Chain C1–C7 · Vizrt Integration C8–C10	Access & Security C20–C24	+15 → 27
S3	5–6	Core: Control Room + ORA Setup	Control Room C11–C16 · AI Content C17–C19 · Performance C25–C29	ORA System Setup O1–O8	+22 → 49
S4	7–8	ORA Live + UAT	Live Results O9–O15 · Interactive	Preparations O23–O25 · Breaking	+15 → 64

Sprint	Weeks	Focus	Dev 1 (TM + Senior)	Dev 2 (Senior)	Features
			Map O16–O18	O30–O31 · UAT	

R1: End of Week 8 — Election-ready broadcast platform

Stretch in Sprint 4 (if capacity): ORA Entity Profiles O19–O22 + Social Sentiment O26–O29 = +8 → 72

Phase 2 — ARENA Sports + FLASH Breaking News (Weeks 9–16)

ARENA and FLASH are built in parallel. Dev 1 owns ARENA. Dev 2 owns FLASH. TM covers architecture review and integration.

Sprint	Weeks	Dev 1 — ARENA	Dev 2 — FLASH	Features
S5	9–10	ORA completion (if needed) · ARENA System Setup A1–A7	FLASH System Setup B1–B4 · Breaking Detection + Alert Queue B5–B6	+19 → 83
S6	11–12	ARENA Live Match A8–A13 · Entity Profiles A14–A16	Multi-Source Aggregation + Verification B7–B11	+16 → 99
S7	13–14	Competition Context A17–A20 · Social A21–A23 · Breaking A24–A25	Ticker B12 · Flash Overlay B13 · Editorial Chain B14–B16	+14 → 113
S8	15–16	QA · UAT · Integration testing	QA · UAT · Cross-module	— → 113

Sprint	Weeks	Dev 1 — ARENA	Dev 2 — FLASH	Features
			breaking feed test	

R2: End of Week 16 — Elections · Sports graphics · Breaking news

Phase 3 — PULSE Finance + ATMOS Weather + Platform Completion (Weeks 17–24)

PULSE and ATMOS are built in parallel. Dev 1 owns PULSE. Dev 2 owns ATMOS. Sprints 11–12 are dedicated to full-platform QA and sign-off.

Sprint	Weeks	Dev 1 — PULSE	Dev 2 — ATMOS	Features
S9	17–18	System Setup F1–F5 · Live Market Data F6– F12	System Setup W1– W4 · Live Weather W5–W10	+22 → 135
S10	19–20	Entity Profiles F13–F14 · Social F15–F16 · Breaking F17–F18	Breaking News W11– W12	+8 → 143
S11	21–22	Platform- wide QA · ≤4 second SLA validation across all 5 modules	Security audit · RBAC verification per role	— → 143
S12	23–24	Full UAT per module · client sign-off	Production hardening · deployment validation	— → 143

Sprint	Weeks	Dev 1 — PULSE	Dev 2 — ATMOS	Features
		per module		

R3: End of Week 24 — Full 5-module broadcast platform

6. Feature Master Plan — All 210 Features

Phase and Delivery Assignment

Module	Feature Group	P1	P2	P3	Delivery Phase	Sprint(s)
Sentra Engine	All capabilities	—	—	—	Foundation	S1
	10-Language NLP (E1)	∞				
	Sentiment + Emotion (E2–E3)	∞				
	NER + AI Generation (E4–E5)	∞				
	Real-Time Pipeline (E6)	∞				
	Breaking + Anomaly (E7–E8)	∞				
	Arabic Processing (E9)	∞				
	Multi-Model AI (E10)	∞				
	Velocity + Credibility (E11–E12)	∞				
Reson8 Core	Editorial Chain (C1–C7)	7			Phase 1	S2
	Vizrt Integration (C8–C10)	3			Phase 1	S2
	Access & Security (C20–C24)	5			Phase 1	S2
		6			Phase 1	S3

Module	Feature Group	P1	P2	P3	Delivery Phase	Sprint(s)
ORA Elections	Control Room (C11–C16)					
	AI Content — P1 (C17–C19)	3			Phase 1	S3
	Performance & Reliability (C25–C29)	∞			Phase 1	S3
	Ticker Copy Generation (C30)		1		Post-R3	—
	Commentary Talking Points (C31)		1		Post-R3	—
	Multi-Output Management (C32)		1		Post-R3	—
	Third Language Output / French (C33)		1		Post-R3	—
	System Setup (O1–O8)	8			Phase 1	S3
	Live Results (O9–O15)	7			Phase 1	S4
	Interactive Map — P1 (O16–O18)	3			Phase 1	S4
	Election Preparations (O23–O25)	3			Phase 1	S4
	Breaking News — P1 (O30–O31)	2			Phase 1	S4
	Entity Profiles — P1 (O19–O22)	4			Phase 1	S4–S5
	Social Sentiment — P1 (O26–O29)	4			Phase 1	S4–S5
	Interactive Map — P2 (O32–O34)		3		Post-R3	—
	Coalition Modelling (O38–O41)		4		Post-R3	—
	AI Prediction Engine (O44–O48)		5		Post-R3	—

Module	Feature Group	P1	P2	P3	Delivery Phase	Sprint(s)
ARENA Sports	AI-Generated Briefs (O35–O37)		3		Post-R3	—
	Track Record (O42–O43)		2		Post-R3	—
	Viral Claim Detection (O49–O50)		2		Post-R3	—
	Breaking — P2 (O51–O52)		2		Post-R3	—
	Constituency Service Record (O53)			1	Future	—
	Social-to-Results Correlation (O54)			1	Future	—
	Storytelling Package (O55–O57)			3	Future	—
	System Setup (A1–A7)	7			Phase 2	S5
	Live Match — P1 (A8–A13)	6			Phase 2	S6
	Entity Profiles — P1 (A14–A16)	3			Phase 2	S6
	Competition Context (A17–A20)	4			Phase 2	S7
	Social Sentiment — P1 (A21–A23)	3			Phase 2	S7
	Breaking News — P1 (A24–A25)	2			Phase 2	S7
	Live Match — P2 xG + Heatmap (A26–A28)		3		Post-R3	—
	AI-Generated Match Brief (A29)		1		Post-R3	—
	Match Outcome Probability (A30–A31)		2		Post-R3	—
	Transfer & Injury Intelligence (A32–A33)		2		Post-R3	—

Module	Feature Group	P1	P2	P3	Delivery Phase	Sprint(s)
PULSE Finance	Viral Moment Detection (A34)		1		Post-R3	—
	Post-Match + Season Stories (A35–A37)			3	Future	—
	System Setup (F1–F5)	5			Phase 3	S9
	Live Market Data (F6–F12)	7			Phase 3	S9
	Entity Profiles (F13–F14)	2			Phase 3	S10
	Social Sentiment (F15–F16)	2			Phase 3	S10
	Breaking News (F17–F18)	2			Phase 3	S10
	Advanced Charts + Watchlist (F19–F21)		3		Post-R3	—
	Economic Calendar + Earnings (F22–F23)		2		Post-R3	—
	Market Sentiment Score (F24)		1		Post-R3	—
ATMOS Weather	Market Stories (F25–F26)			2	Future	—
	System Setup (W1–W4)	4			Phase 3	S9
	Live Weather (W5–W10)	6			Phase 3	S9
	Breaking News (W11–W12)	2			Phase 3	S10
	Animated Maps + Radar (W13–W14)		2		Post-R3	—
	Extended Forecasts + UV + Wind (W15–W18)		4		Post-R3	—
	Historical + Climate Stories (W19–W21)			3	Future	—

Module	Feature Group	P1	P2	P3	Delivery Phase	Sprint(s)
FLASH Breaking	System Setup (B1–B4)	4			Phase 2	S5
	Live Breaking + Editorial (B5–B16)	12			Phase 2	S6–S7
	Story Priority + Clustering (B17–B20)		4		Post-R3	—
	Timeline + Crisis Reconstruction (B21–B22)			2	Future	—

7. Product Build-Up Curve

Cumulative Features by Sprint

Sprint	Week	Features Added	Cumulative	Broadcast Capability
S1 — Foundation	2	12	12	— Infrastructure only
S2 — Core Part 1	4	15	27	— Core building
S3 — Core Complete + ORA Setup	6	22	49	— Platform ready, no module live yet
S4 — ORA Live	8	15	64	✓ Elections — live results · map · editorial chain
S5 — ORA Complete + Module Setups	10	19	83	✓ Elections (full)
S6 — ARENA Live +	12	16	99	✓ Elections · Sports graphics ·

Sprint	Week	Features Added	Cumulative	Broadcast Capability
FLASH Detection				Breaking detection
S7 — ARENA + FLASH Complete	14	14	113	✓ Elections · Sports graphics · Breaking news on air
S8 — QA + UAT	16	—	113	✓ R2: 3 modules broadcast-ready
S9 — PULSE + ATMOS Live	18	22	135	✓ All 5 modules — initial release
S10 — PULSE + ATMOS Complete	20	8	143	✓ All 5 modules — full feature set
S11 — Platform QA	22	—	143	✓ SLA validated · security audited
S12 — UAT + Sign-off	24	—	143	✓ R3: Full platform production-ready

Visual Curve

Cumulative Features (■ = 5 features)

Wk 2 ■■	12	
Foundation		
Wk 4 ■■■■	27	
Core Part 1		
Wk 6 ■■■■■■■■	49	
Core Complete		
Wk 8 ■■■■■■■■■■ ◀ R1 Elections Live	64	
Wk 10 ■■■■■■■■■■■■	83	+
ORA Full + Module Setups		
Wk 12 ■■■■■■■■■■■■■■	99	+
ARENA + FLASH Mid		

Wk 14			113	+
ARENA + FLASH Complete				
Wk 16		◀ R2 3 Modules Live	113	QA
Sprint				
Wk 18			135	+
PULSE + ATMOS Live				
Wk 20			143	
All 5 Modules Complete				
Wk 22			143	
Platform QA				
Wk 24		◀ R3 Full	143	
Production Ready				

Capability Progression

Release	Month	Modules	What broadcasts are covered
R1	2	Core + ORA	Any election broadcast — results, map, seat tally, social sentiment
R2	4	+ ARENA + FLASH	Elections + any live sports match + any breaking news event
R3	6	+ PULSE + ATMOS	Full platform — elections · sports · markets · weather · breaking

8. Phase Summaries

Phase 1 – Foundation + Core + ORA Elections

Month 1-2 · 4 sprints · 64 features committed

The most technically significant phase. Every line of architecture written here shapes the platform for three years.

Sprint 1 is not about features — it is about correctness. Module registry, FAL, event pipeline, entity model, Sentra Engine client, and Vizrt template registry must all be designed for five modules, not one.

Sprint 2–3 complete the Reson8 Core — 29 features shared by all modules, built once.

Sprint 4 brings ORA live. By end of Week 8 the platform can ingest an official election results feed, route each result through the editorial chain, generate a bilingual graphic, and fire it to a Vizrt renderer in under 4 seconds.

Phase 2 — ARENA Sports + FLASH Breaking News

Month 3–4 · 4 sprints · +49 features

The two modules run in parallel. ARENA is data-driven (structured feed from Opta/Stats Perform). FLASH is signal-driven (unstructured detection from social and wire). They share nothing except the Core editorial chain — which is already built.

By end of Week 16, the platform covers every live sports match event (goal, card, substitution, VAR, stats, standings) and classifies breaking news across 10 languages in real time before surfacing it to the editorial queue.

Phase 3 — PULSE Finance + ATMOS Weather + Platform Completion

Month 5–6 · 4 sprints · +30 features + QA

PULSE and ATMOS are the lowest-risk phase. Core is proven across 3 modules. The Feed Abstraction Layer has handled elections results APIs (O5), Opta (A5), and news wire APIs (B1). Plugging in Bloomberg/Reuters (F3) and Tomorrow.io (W2) is configuration, not architecture.

Sprints 11–12 are reserved entirely for: - Platform-wide SLA validation (≤ 4 seconds, all 5 modules, under load) - Security audit and RBAC verification - Full UAT per module - Production deployment validation

By end of Week 24: 143 features delivered, 5 modules live, platform production-ready.

9. Post-R3 — Intelligence Layer

After R3, the platform enters its intelligence phase. 67 additional features across P2 and P3.

P2 — Intelligence Layer (52 features)

Module	Feature Groups	Features
Core	Ticker Copy ·	4
	Commentary	
	Talking Points ·	
	Multi-Output ·	
	French Output	
ORA	AI Predictions ·	21
	Coalition	
	Modelling · Swing	
	Maps · AI Briefs ·	
	Track Record ·	
ARENA	Viral Detection	10
	xG · Heatmaps ·	
	Match Outcome	
	Probability ·	
	Transfer	
PULSE	Intelligence · Viral	7
	Moments	
	Advanced Charts ·	
	Economic	
	Calendar ·	
ATMOS	Earnings	6
	Dashboard ·	
	Market Sentiment	
	Animated Maps ·	
	Radar · Extended	
FLASH	Forecast · Wind	4
	Map · UV Map	
	Story Priority ·	
	Clustering ·	
	Escalation	
Total P2	Detection ·	52
	Archive	

P3 — Storytelling & Distribution (15 features)

Module	Feature Groups	Features
ORA	Election Night Story Builder · Post-Election Analysis · Historical Trend Analysis · Social- to-Results Correlation · Constituency Service Record	5
ARENA	Post-Match Package · Season Deep Dive · Historical Records	3
PULSE	Market Story Builder · IPO / Earnings Tracker	2
ATMOS	Historical Weather Comparison · Climate Trend · Weather Impact Stories	3
FLASH	Breaking News Timeline Builder · Crisis Reconstruction	2
Total P3		15

10. Definition of Done — Each Release

R1 Complete when:

- Full editorial chain tested end-to-end: Producer → Editor → Operator → Vizrt → On-air
- Live election results feed ingested, validated, and on screen in ≤4 seconds
- Geographic results map live with party colour fills
- Arabic + English bilingual output validated

- RBAC verified per role (Producer / Editor / Operator / Admin)
- UAT signed off on all ORA P1 features

R2 Complete when:

- ARENA: live match data (score · events · stats) on air in ≤4 seconds from official feed
- FLASH: breaking event detected, classified, surfaced to editorial queue, and on air within editorial SLA
- Cross-module editorial chain tested (ORA + ARENA + FLASH simultaneously)
- All 3 modules passing UAT

R3 Complete when:

- All 143 P1 features implemented and passing acceptance criteria
- ≤4 second wire-to-air SLA validated under load across all 5 modules
- Security audit passed
- 99.99% uptime architecture verified
- All 10 languages processing correctly through the Engine
- UAT signed off per module
- Production deployment validated on-premises or cloud per client requirement
